


ClassMic WBS and Schedule

Temiko Machavariani and Nurtore Arynuruly
BUS 2010 17 September 2026 ABCDEF work breakdown and proposed schedule

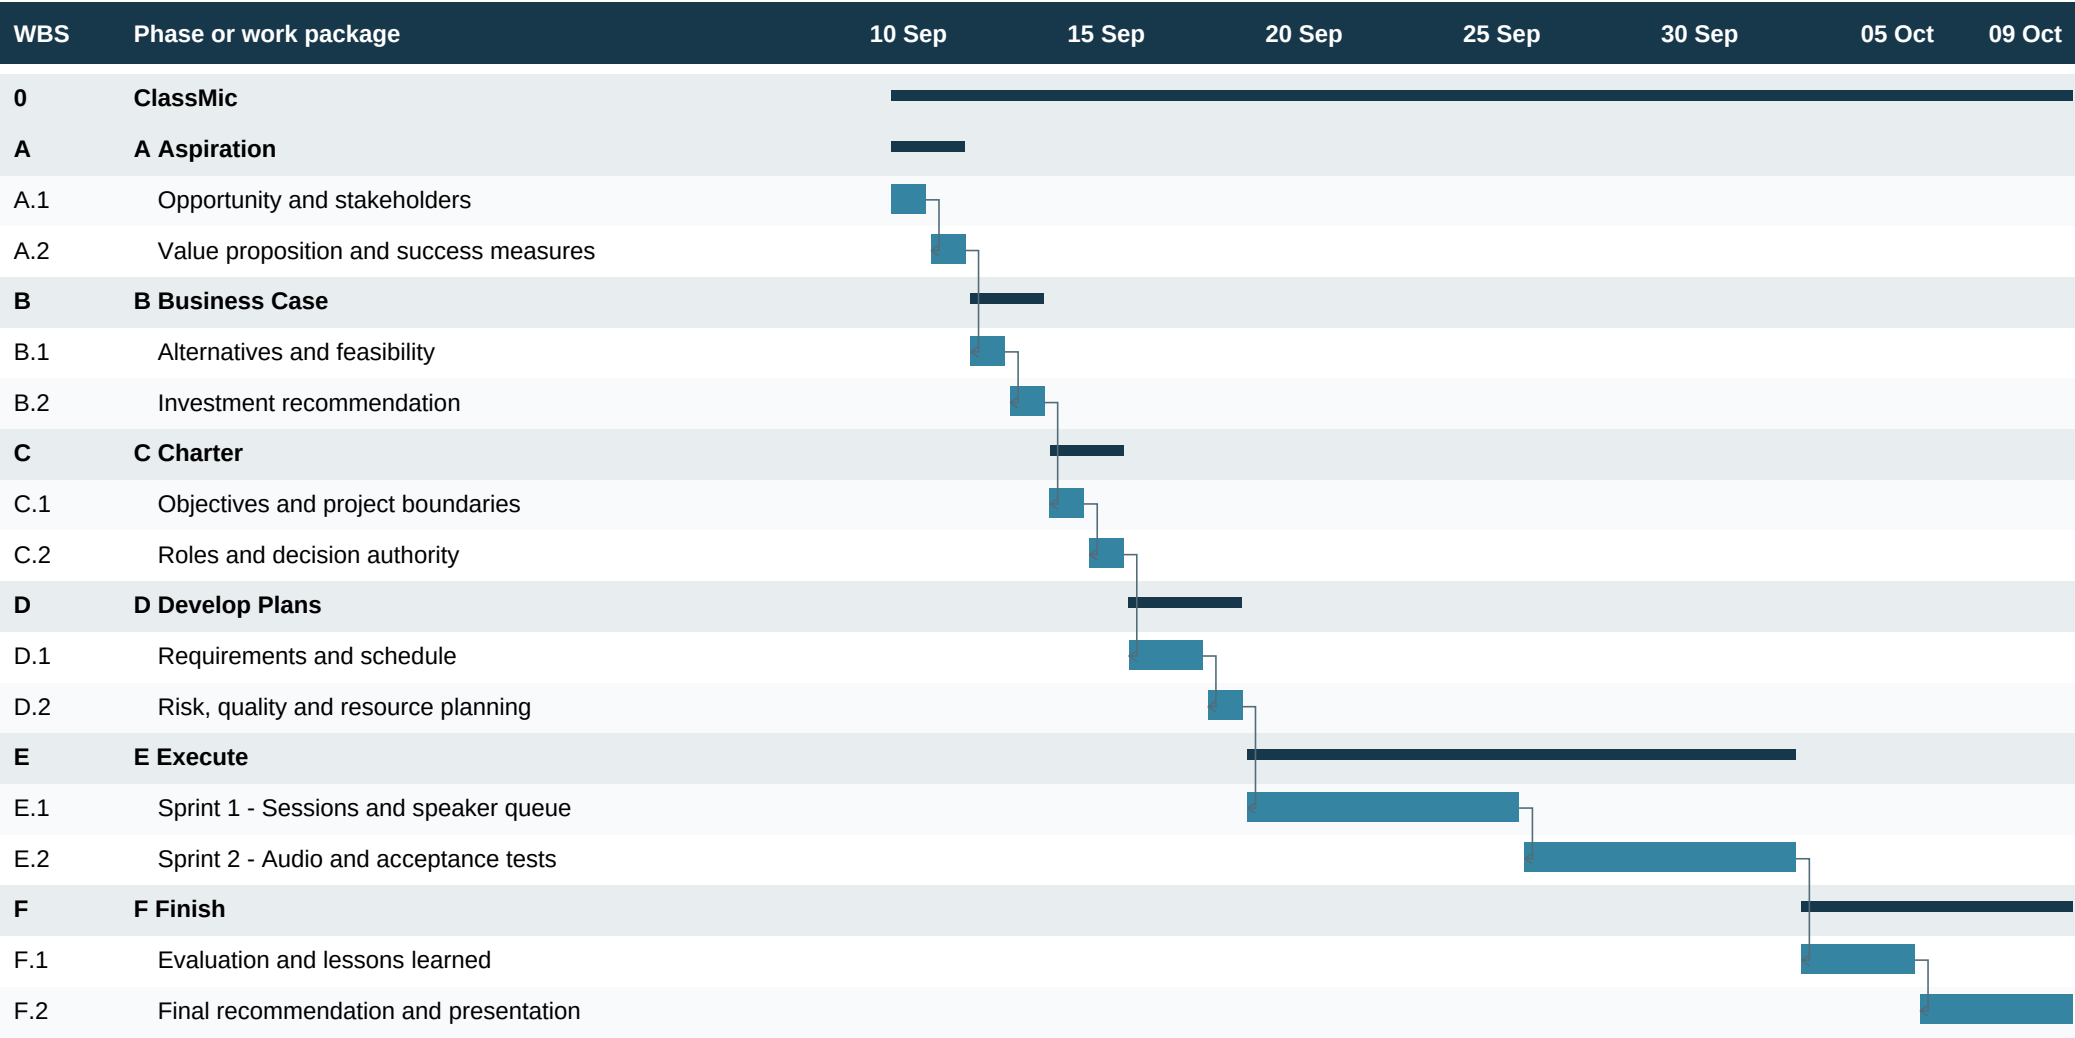

19 WBS elements: one project root, six phases and 12 work packages. Dependencies are finish-to-start with zero lag.
The calendar includes all seven days of the week. Each development sprint lasts seven days.
Estimated effort: 100 student hours across 30 calendar days.

ClassMic WBS and Schedule

Temiko Machavariani and Nurtore Arynuruly

BUS 2010 17 September 2026 Work estimates and deadlines

ID	WBS	Work package	Days	Start	Finish	Pred	Temiko h	Nurtore h	Total h
3	A.1	Opportunity and stakeholders	1	10 Sep	10 Sep	-	1	3	4
4	A.2	Value proposition and success measures	1	11 Sep	11 Sep	3	1	3	4
6	B.1	Alternatives and feasibility	1	12 Sep	12 Sep	4	2	2	4
7	B.2	Investment recommendation	1	13 Sep	13 Sep	6	2	2	4
9	C.1	Objectives and project boundaries	1	14 Sep	14 Sep	7	2	2	4
10	C.2	Roles and decision authority	1	15 Sep	15 Sep	9	2	2	4
12	D.1	Requirements and schedule	2	16 Sep	17 Sep	10	4	4	8
13	D.2	Risk, quality and resource planning	1	18 Sep	18 Sep	12	4	4	8
15	E.1	Sprint 1 - Sessions and speaker queue	7	19 Sep	25 Sep	13	18	6	24
16	E.2	Sprint 2 - Audio and acceptance tests	7	26 Sep	02 Oct	15	14	10	24
18	F.1	Evaluation and lessons learned	3	03 Oct	05 Oct	16	2	4	6
19	F.2	Final recommendation and presentation	4	06 Oct	09 Oct	18	2	4	6
Total effort							54	46	100

Dependencies. The phases follow A, B, C, D, E and F. Within each phase, package 1 precedes package 2. The final package in each phase must finish before the next phase begins. A delay on this sequence delays the planned finish.

Calendar and effort. Working windows are 08:00-12:00 and 13:00-17:00 every day. Each duration day represents eight scheduling hours. Estimated work is allocated separately: 54 hours for Temiko and 46 for Nurtore, distributed across those windows.

Deadlines. The plan review target is 18 September. Course deadlines are 22 September for planning, 3 October for the product report, 4 October for execution evidence and 10 October for the final presentation, all at 00:00.

Assumptions. The team can provide the estimated hours, equipment and volunteer reviewers are available, and the instructor accepts the proposed sequence. New spending or live classroom use would require separate approval.
