


ClassMic WBS and Schedule

Temiko Machavariani and Nurtore Arynuruly

BUS 2010 17 September 2026 ABCDEF work breakdown and linked baseline

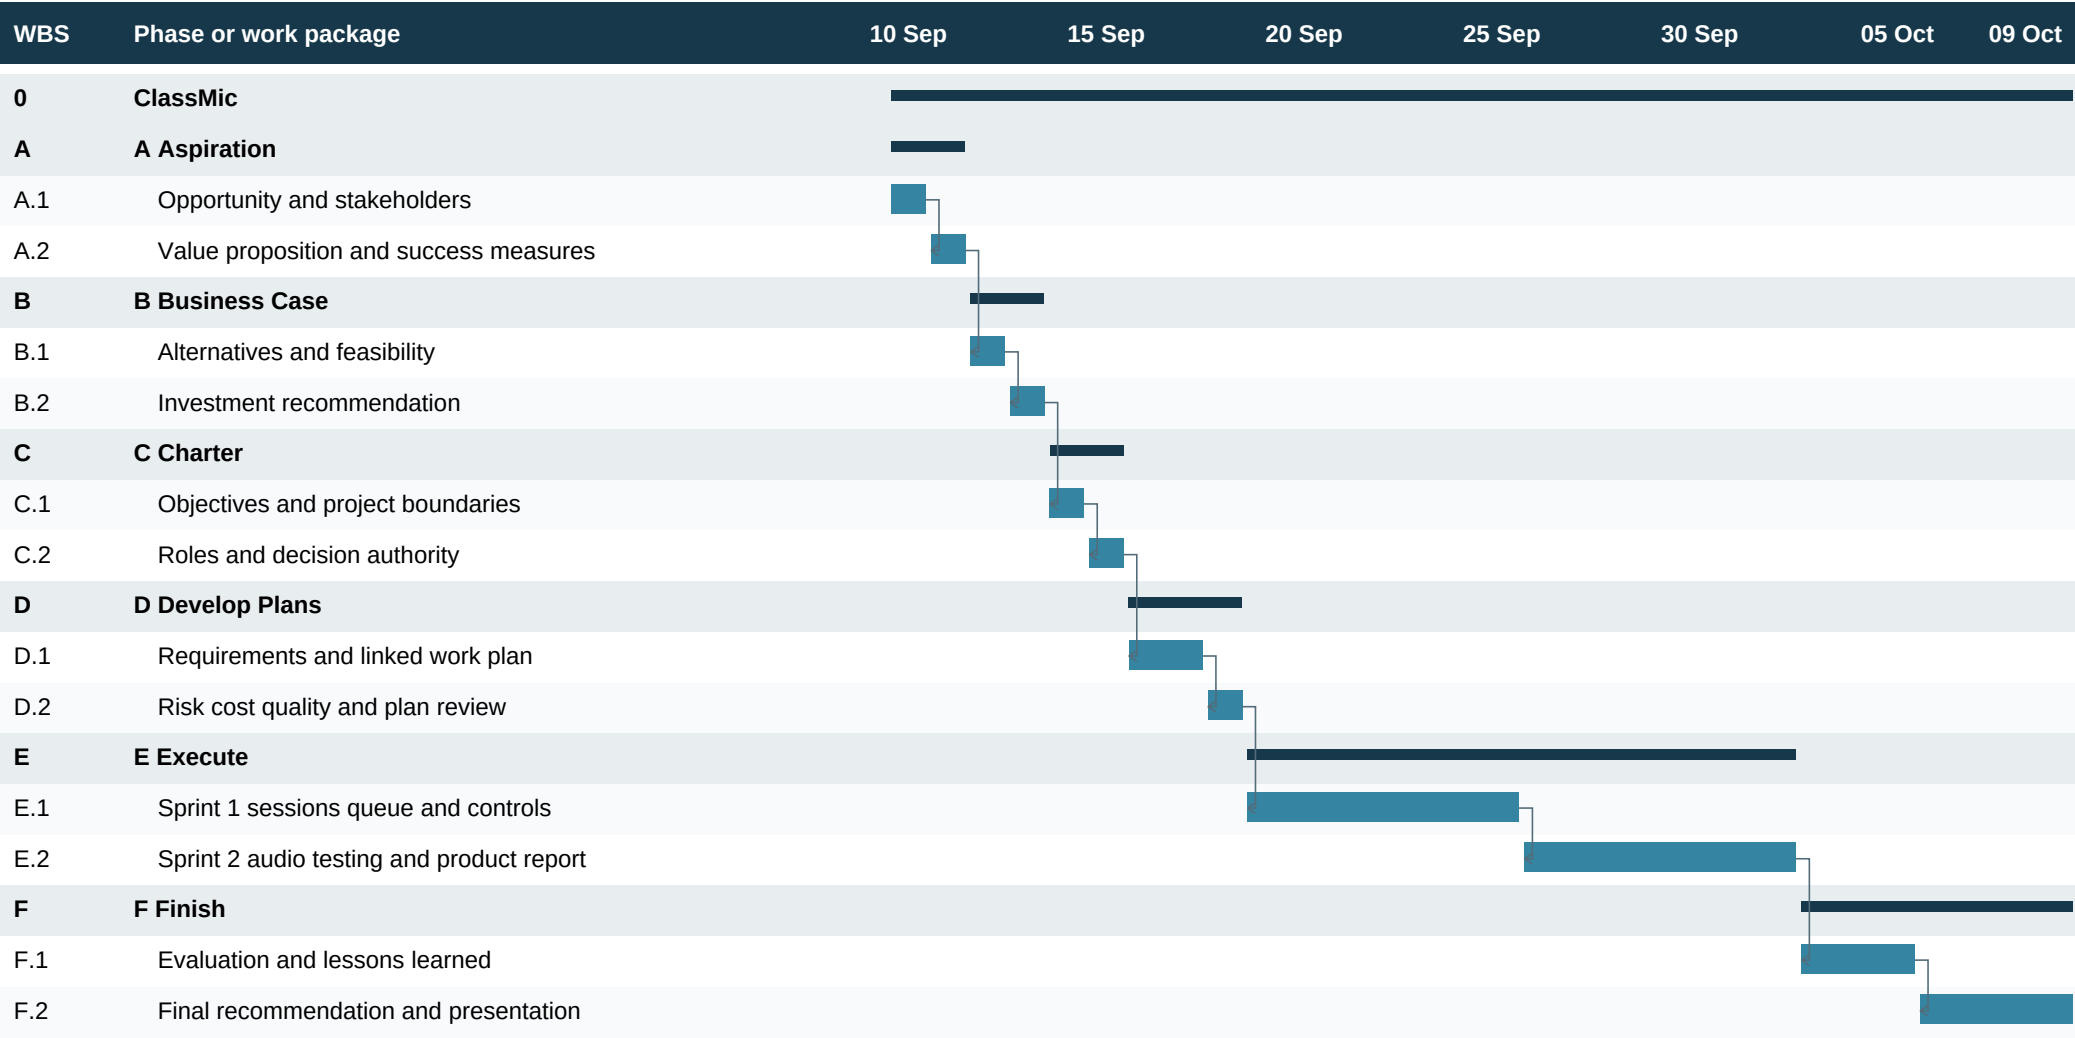

19 WBS elements: one project root, six phases and 12 linked work packages. All dependencies are finish-to-start with zero lag.

The 30-day baseline uses a seven-day calendar. Each build sprint spans seven days; effort totals 100 student hours.

Dates and effort are planning estimates. This schedule does not report completed project work.

ClassMic WBS and Schedule

Temiko Machavariani and Nurtore Arynuruly

BUS 2010 17 September 2026 Durations responsibilities and constraints

ID	WBS	Work package	Days	Start	Finish	Pred	Temiko h	Nurtore h	Total h
3	A.1	Opportunity and stakeholders	1	10 Sep	10 Sep	-	1	3	4
4	A.2	Value proposition and success measures	1	11 Sep	11 Sep	3	1	3	4
6	B.1	Alternatives and feasibility	1	12 Sep	12 Sep	4	2	2	4
7	B.2	Investment recommendation	1	13 Sep	13 Sep	6	2	2	4
9	C.1	Objectives and project boundaries	1	14 Sep	14 Sep	7	2	2	4
10	C.2	Roles and decision authority	1	15 Sep	15 Sep	9	2	2	4
12	D.1	Requirements and linked work plan	2	16 Sep	17 Sep	10	4	4	8
13	D.2	Risk cost quality and plan review	1	18 Sep	18 Sep	12	4	4	8
15	E.1	Sprint 1 sessions queue and controls	7	19 Sep	25 Sep	13	18	6	24
16	E.2	Sprint 2 audio testing and product report	7	26 Sep	02 Oct	15	14	10	24
18	F.1	Evaluation and lessons learned	3	03 Oct	05 Oct	16	2	4	6
19	F.2	Final recommendation and presentation	4	06 Oct	09 Oct	18	2	4	6
Total effort							54	46	100

Dependency chain. A.1 to A.2 to B.1 to B.2 to C.1 to C.2 to D.1 to D.2 to E.1 to E.2 to F.1 to F.2. The serial chain controls the baseline finish. Summary phases roll up their children and carry no duplicate dependency links.

Calendar and effort. Working windows are 08:00-12:00 and 13:00-17:00 every day. A duration day is an eight-hour scheduling window, not eight hours assigned to each person. Resource assignments distribute the separate effort estimates across those windows.

Release constraints. Plan review target: 18 September. Planning submission: 22 September at 00:00. Sprint 1: 19-25 September. Sprint 2: 26 September-2 October. Product report: 3 October at 00:00. Execution evidence: 4 October at 00:00. Final presentation: 10 October at 00:00.

Assumptions. Both team members can provide the estimated effort, existing equipment is available, and the instructor accepts the proposed sequencing. Review scope and dates if these assumptions fail. No paid resources or live classroom deployment are authorized.
