


ClassMic WBS and Schedule

Temiko Machavariani and Nurtore Arynuruly
BUS 2010 17 September 2026 ABCDEF work breakdown and proposed schedule

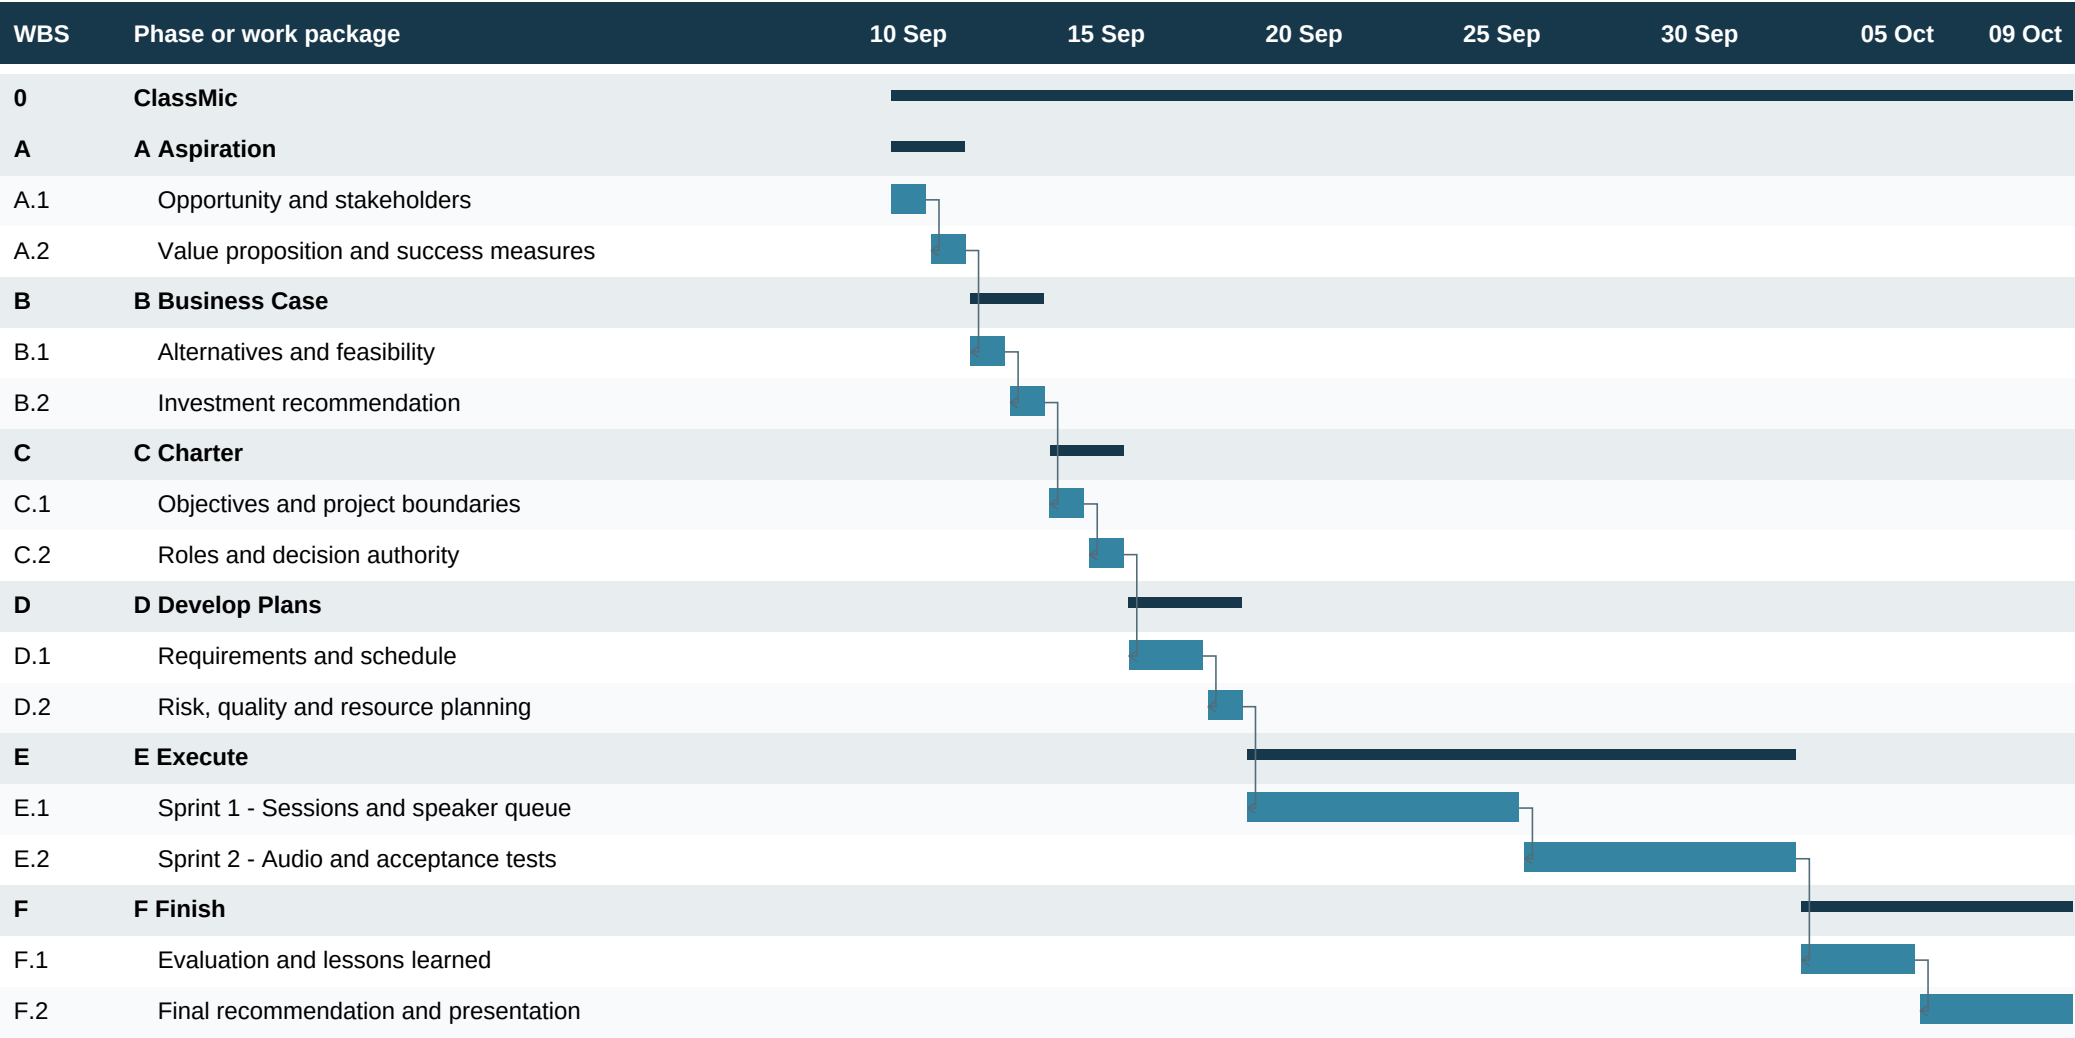

19 WBS elements: one project root, six phases and 12 work packages. Dependencies are finish-to-start with zero lag.
Both sprints use Temiko Machavariani, Nurtore Arynuruly, Computer and AI tools.
Estimated student effort: 100 hours. The seven-day calendar gives each sprint seven consecutive days.

ClassMic WBS and Schedule

Temiko Machavariani and Nurtore Arynuruly

BUS 2010 17 September 2026 Student effort and sprint resources

ID	WBS	Work package	Days	Start	Finish	Pred	Temiko h	Nurtore h	Total h
3	A.1	Opportunity and stakeholders	1	10 Sep	10 Sep	-	1	3	4
4	A.2	Value proposition and success measures	1	11 Sep	11 Sep	3	1	3	4
6	B.1	Alternatives and feasibility	1	12 Sep	12 Sep	4	2	2	4
7	B.2	Investment recommendation	1	13 Sep	13 Sep	6	2	2	4
9	C.1	Objectives and project boundaries	1	14 Sep	14 Sep	7	2	2	4
10	C.2	Roles and decision authority	1	15 Sep	15 Sep	9	2	2	4
12	D.1	Requirements and schedule	2	16 Sep	17 Sep	10	4	4	8
13	D.2	Risk, quality and resource planning	1	18 Sep	18 Sep	12	4	4	8
15	E.1	Sprint 1 - Sessions and speaker queue	7	19 Sep	25 Sep	13	18	6	24
16	E.2	Sprint 2 - Audio and acceptance tests	7	26 Sep	02 Oct	15	14	10	24
18	F.1	Evaluation and lessons learned	3	03 Oct	05 Oct	16	2	4	6
19	F.2	Final recommendation and presentation	4	06 Oct	09 Oct	18	2	4	6
Total student effort							54	46	100

Dependencies. The phases follow A, B, C, D, E and F. Within each phase, package 1 precedes package 2. The final package in each phase must finish before the next phase begins. A delay on this sequence delays the planned finish.

Resources and calendar. Temiko and Nurtore provide 100 estimated student hours. Computer and AI tools are assigned to both sprint packages, E.1 and E.2, using existing equipment and tool access. Duration uses eight-hour calendar days; student work is estimated separately.

Deadlines. The plan review target is 18 September. Course deadlines are 22 September for planning, 3 October for the product report, 4 October for execution evidence and 10 October for the final presentation, all at 00:00.

Assumptions. The team can provide the estimated hours, equipment and volunteer reviewers are available, and the instructor accepts the proposed sequence. New spending or live classroom use would require separate approval.
